



The Moorings Condominiums Building 4

350 - 364 Moorings Cove Drive
Tarpon Springs, FL 34689
B.A.S.I.C. File No.: B2020-018

March 25th, 2021



FINAL REPORT



Bay Area Sinkhole Investigation & Civil Engineering

2601 E. 7th Avenue, Tampa, FL 33605

Ph: (813) 885-4144 | Fx: (813) 885-4166

www.basic-engineering.com

To: The Moorings Condominiums Association Date: 03/25/2021
Attn: Karen Cleary, President Project # B2020-018
450 Moorings Cove Drive
Tarpon Springs, FL 34689

Subject: Injection Pin Pile, Compaction and Chemical Grouting
The Moorings Condominiums | Building 4
350 – 364 Moorings Cove Drive, Tarpon Springs, FL 34689

Dear Ms. Cleary,

We have reviewed a Structural Damage Evaluation and Subsidence Investigation report by SDII Global, (SDII), dated April 6th, 2018, a Geologic/Geotechnical Testing and Evaluation report by Applied Engineering & Geosciences (AEG), dated September 22nd, 2018, a Sinkhole Loss Determination report by Structural Engineering and Inspections, Inc, (SEI), dated November 28th, 2018, a Peer Review report by SDII Global, (SDII), dated January 11th, 2019, a Neutral Evaluation report by Andreyev Engineering, Inc., (AEI), dated March 16th, 2020 and field work and engineering design performed by B.A.S.I.C. Engineering.

Based on the aforementioned reports, you have asked us to recommend and monitor a remediation program. B.A.S.I.C. Engineering recommended utilizing a combination of injection pin piles, compaction grouting and chemical grouting points. We have provided you with a Site Plan indicating the location of the injection pin piles, compaction grout and chemical grouting points and their estimated depths of installation. However, we were unable to accurately predict the amount of grout that would be required prior to actual field installation.

Injection Pin Piles are recommended in similar situations whereby the property requires lifting or other foundation support in addition to sealing off the limestone interface to prevent future sinkhole activity from occurring. The installation of the Injection Pin Piles is a process whereby high carbon steel pilings are hydraulically driven into the ground until a predetermined pressure reading is attained, or refusal occurs where lifting of the structure takes place. The Injection Pin Piles are then grouted through a patented process allowing grout to be pumped directly at the limestone interface.

In addition to the installation of the Injection Pin Piles, a high slump pressure grouting program is recommended as a means of sealing deep openings into underlying cavernous zones, fill in void zones, consolidate/densify the loose soils, prevent downward migration of soil particles and also to provide greater lateral stability to the steel pilings. A 4-6 inch slump grout is recommended by B.A.S.I.C. Engineering so that it may be accurately pumped below the structure and it may flow through the grout holes and densify soil voids with greatest efficiency.

Compaction grouting is the injection of grout into the soil to improve bearing capacity. This is accomplished by using a very viscous (low-mobility), aggregate under high pressure to form grout bulbs, which displace and densify the surrounding soils in a controlled manner through an injection pipe. The upward component of force causing heaving at the surface during compaction grouting usually limits the degree which soil can be compacted, making compaction grouting ineffective for stabilizing upper level soils (approximately the top 15 feet). Therefore, in order to stabilize the uppermost subsurface soils, chemical grouting has also been recommended.

Chemical grouting is a process whereupon a polyurethane grout is injected to fill void spaces and improve the strength of granular soils. Chemical grout behaves like a fluid but reacts with an agent and water and within sixty seconds forms a solid, expanding to compact the soils similarly to standard compaction grouting but in a more controlled manner.

MONITORING

As requested, we have completed the monitoring of the subsurface injection pin piles, compaction grouting and chemical grouting operations as conducted by Helicon Foundation Repair Systems, Inc., (Helicon). This work was completed utilizing the TMG Injection Pier System, Compaction Grouting and Chemical Grouting. The remediation was started on February 2nd, 2021 and completed on March 15th, 2021. A technician from our firm was present during the remediation operations to monitor operations and perform applicable grout slump tests.

Helicon installed a total of 66 injection pin piles around the property as per our site plan recommendations, as shown in figure 4a. Due to the site conditions, four (4) point were omitted from our original recommendations. (Injection Pin Pile Numbers 7, 19, 28 and 51). The depths of installation ranged from a low of 5 feet to a high of 160 feet below grade. Each pin pile was hydraulically driven into the soil until enough pressure was reached for refusal. The hydraulic gauge reading (psi) was recorded for each injection pin pile along with the installed depth (Figure 4b). The contractor then accepted delivery of a 1500-psi pressure grout from Pasco Ready Mix. The grout was a high slump 4-6 inch pressure grout. A grout gun was connected to each of the 66 injection pin piles pumped by Helicon, utilizing a TK-40 pump. The grout was pumped until a pressure gauge reading of up to 400-psi was reached on the in-line gauge. The amount of grout pumped for each injection pin pile was recorded (Figure 4a). A total of 28.4 cubic yards of grout was pumped in various quantities through 66 injection pin piles points.


Helicon then staked the compaction grout point locations as shown in Figure 4c in accordance with B.A.S.I.C. Engineering's recommendations. Angled compaction grout points were installed to refusal (hard limestone bedrock) at depths ranging from 97 to 108 feet below existing grade. A total of 918 feet of grout casing was installed at the 9 compaction grout points. After the grout casing was installed, a TK-40 pump was used to inject a mixture of cement, fly ash, sand, water, and other admixtures into the loose soils and voids in the limestone and overlying sand strata. Pumping continued until a grout pressure of 200 to 400 psi was achieved (over that required to initiate grout take) or lifting of the structure was observed (via a surveyor's level). The grout casing was then extracted upward four to five feet and pumping resumed. A total of 66.3 cubic yards of grout was pumped in various quantities through 9 compaction grout points on the subject property, ranging from a minimum of 1.73 cubic yards on point #5 to a maximum of 12.05 cubic yards on point #2.

Lastly, a total of 836.7 lbs. of chemical grout was injected through 12 chemical grout points by Helicon as shown in Figures 4d. Angled points were pumped at depth ranges between 12', 10', 8', 6', 4' and 2 feet below ground surface until lift of the slab/ground refusal was achieved.

It is our opinion that the injection pin piles, compaction grout and chemical grout were installed in accordance with industry standards and are an effective method to fill voids, cracks, fractures and cavities and to stabilize granular material, thus improving the physical properties of soil and rock at The Moorings Condominiums | Building #4. The proven technology utilized by the pier manufacturer and the ability to solve foundation settlement problems using a combination of injection pin piles, compaction grout and chemical grout, has demonstrated success without additional settlement. This report is not a guarantee that sinkhole activity will not continue to exist at the subject property but rather a summary and certification of the work completed by Helicon Foundation Repair Systems, Inc.

We thank you for the opportunity to provide the services to you on this project. We trust that the information provided in this letter is satisfactory. Should you have any questions, or require additional assistance, please do not hesitate to call.

Sincerely,


A handwritten signature in blue ink, appearing to read 'Justin D. James', followed by the date '3/25/21' written in the same ink.

Justin D. James, P.E.
Florida P.E. # 60886
C.O.A. # 25869
Attachments

TECHNICAL NOTES:

- ⊗ - INJECTION PIN PILE
- ⊗ - SPREADER BEAM
- ⊙ - POINTS OMITTED
- SEE FIGURE 4b FOR INJECTION PIN PILE DETAIL
- NOT FOR PERMITTING

TWO STORY WOOD FRAME BUILDING #4

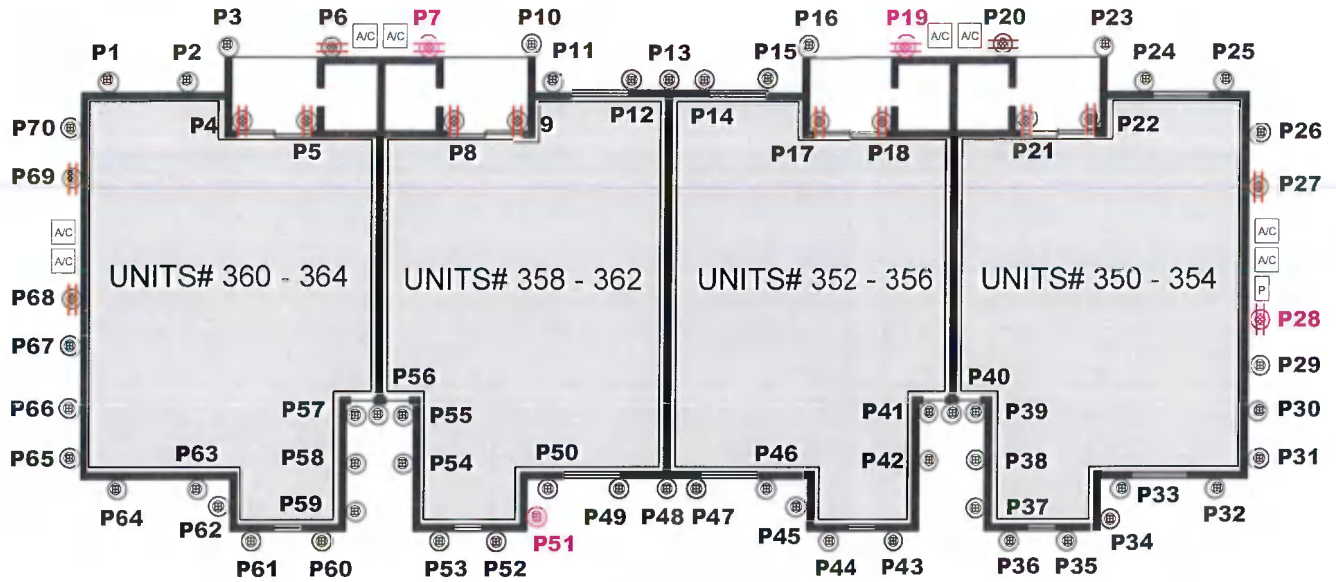

Points #	PSI	Depth (ft)	Strokes	Actual Grout (cy)
1	500	100.0	6	0.11
2	2000	90.0	6	0.11
3	2000	65.0	8	0.15
4	2000	65.0	3	0.05
5	2100	63.0	95	1.66
6	2100	63.0	3	0.05
7	-	-	-	-
8	2100	55.0	128	2.24
9	2100	60.0	3	0.05
10	2000	60.0	2	0.03
11	2100	55.0	1	0.02
12	2200	60.0	1	0.02
13	2000	60.0	5	0.09
14	1200	100.0	46	0.80
15	2300	5.0	2	0.03
16	2000	55.0	37	0.58
17	2000	70.0	93	1.46
18	2000	65.0	121	1.90
19	-	-	-	-
20	2100	55.0	163	2.09
21	2000	54.0	8	0.10
22	2000	50.0	5	0.06
23	2200	55.0	5	0.06

Points #	PSI	Depth (ft)	Strokes	Actual Grout (cy)
24	2500	5.0	3	0.05
25	2500	5.0	3	0.05
26	2000	92.0	59	0.92
27	2100	85.0	2	0.03
28	-	-	-	-
29	2300	90.0	245	4.45
30	2000	80.0	30	0.55
31	2200	85.0	44	0.78
32	2100	75.0	90	1.60
33	2300	75.0	99	1.76
34	2500	85.0	2	0.04
35	2600	100.0	2	0.04
36	2400	92.0	9	0.16
37	2000	54.0	18	0.32
38	2000	50.0	3	0.05
39	2100	57.0	15	0.27
40	2100	55.0	7	0.13
41	2200	55.0	26	0.46
42	2700	90.0	2	0.04
43	2500	90.0	4	0.07
44	2600	93.0	15	0.25
45	2600	100.0	12	0.20
46	2600	110.0	1	0.02
47	2700	110.0	2	0.03

Points #	PSI	Depth (ft)	Strokes	Actual Grout (cy)
48	2700	100.0	6	0.10
49	2600	120.0	4	0.07
50	2800	150.0	2	0.03
51	-	-	-	-
52	2500	110.0	2	0.03
53	2500	147.0	6	0.10
54	2700	115.0	4	0.07
55	2200	65.0	170	3.06
56	2100	75.0	14	0.25
57	2800	129.0	4	0.07
58	2700	155.0	2	0.04
59	2700	155.0	3	0.05
60	2500	154.0	4	0.07
61	2600	155.0	2	0.04
62	2600	154.0	2	0.04
63	2600	132.0	2	0.04
64	2500	125.0	2	0.04
65	2600	119.0	2	0.04
66	2700	116.0	2	0.04
67	2600	125.0	4	0.07
68	2800	160.0	6	0.11
69	2400	120.0	2	0.04
70	2500	118.0	3	0.05
TOTALS:	5837.0	1682	28.4	

Approximate Scale

1" = 20'



BASIC ENGINEERING

2601 E. 7TH AVENUE, TAMPA, FL 33605 | PH: 813-885-4144 * FX: 813-885-4166
WWW.BASIC-ENGINEERING.COM

THE MOORINGS CONDO ASSOC. | BLDG #4

350 - 364 MOORING COVE DRIVE; TARPON SPRING 34689
PINELAS COUNTY

CONSTRUCTION INJECTION PIN PILE PLAN


FIGURE NO.: 4a

FILE NO.: B2020-018

DATE: 03/25/2021

CHECKED BY: JJ

Wood Frame on Spread Footer:
Injection Pin Pile Detail
(Not for Permitting)

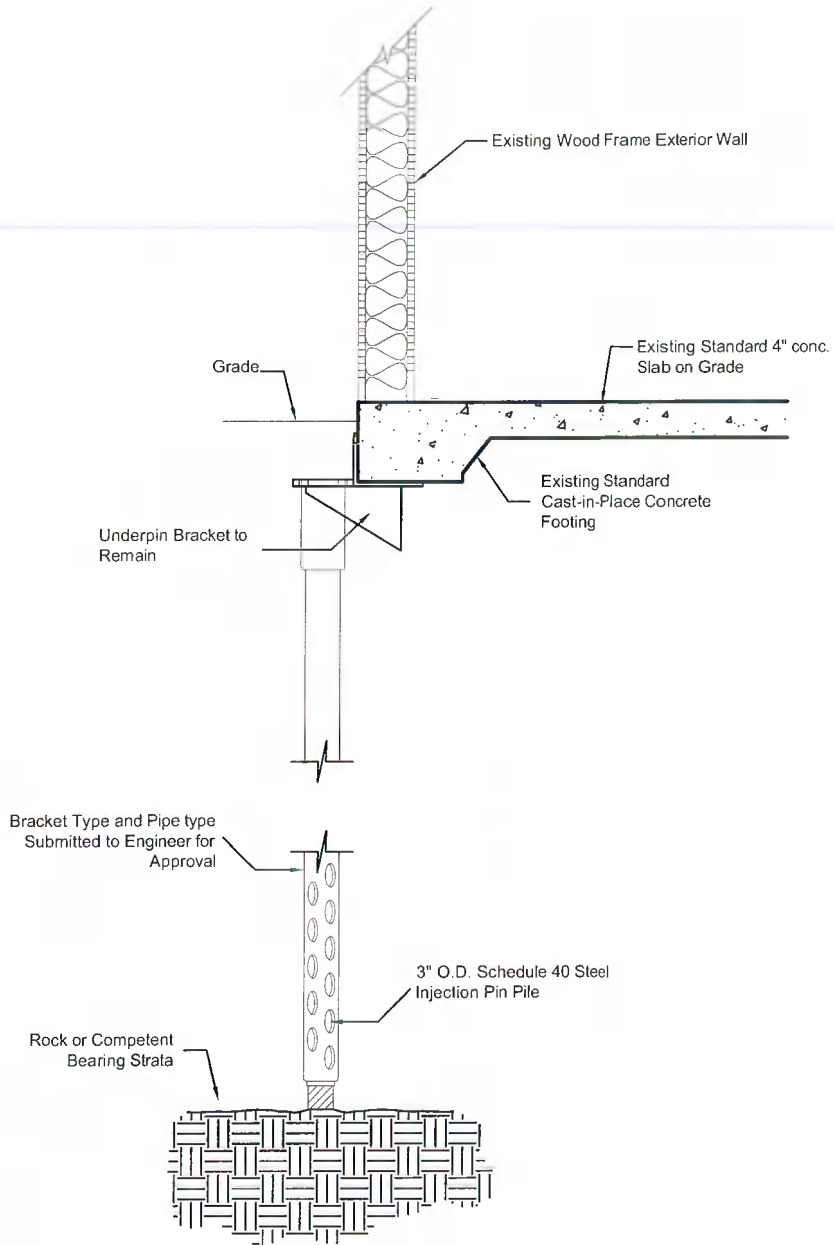

BASIC
ENGINEERING

2601 E 7TH AVENUE, TAMPA, FL 33605 | PH: 813-885-4144 * FX: 813-885-4166
WWW.BASIC-ENGINEERING.COM

THE MOORINGS CONDO ASSOC. | BLDG #4
350 - 364 MOORING COVE DRIVE; TARPON SPRING 34689
PINELAS COUNTY

INJECTION PIN PILE PLAN

FIGURE NO.: 4b

FILE NO.: B2020-018

DATE: 03/25/2021

CHECKED BY: JJ

TECHNICAL NOTES:

- INSTALLED POINTS DEPTHS: 97' - 108'


⊙ = ANGLED COMPACTION GROUT POINT

- NOT FOR PERMITTING




Points #	Depth (ft)	Strokes	Actual Grout (cy)
1	100	367	6.73
2	104	671	12.05
3	104	700	11.95
4	100	443	7.85
5	100	135	1.73
6	108	195	3.09
7	105	487	8.55
8	100	480	8.52
9	97	321	5.83
Total:	918	Total:	66.3

TWO STORY WOOD FRAME BUILDING #4

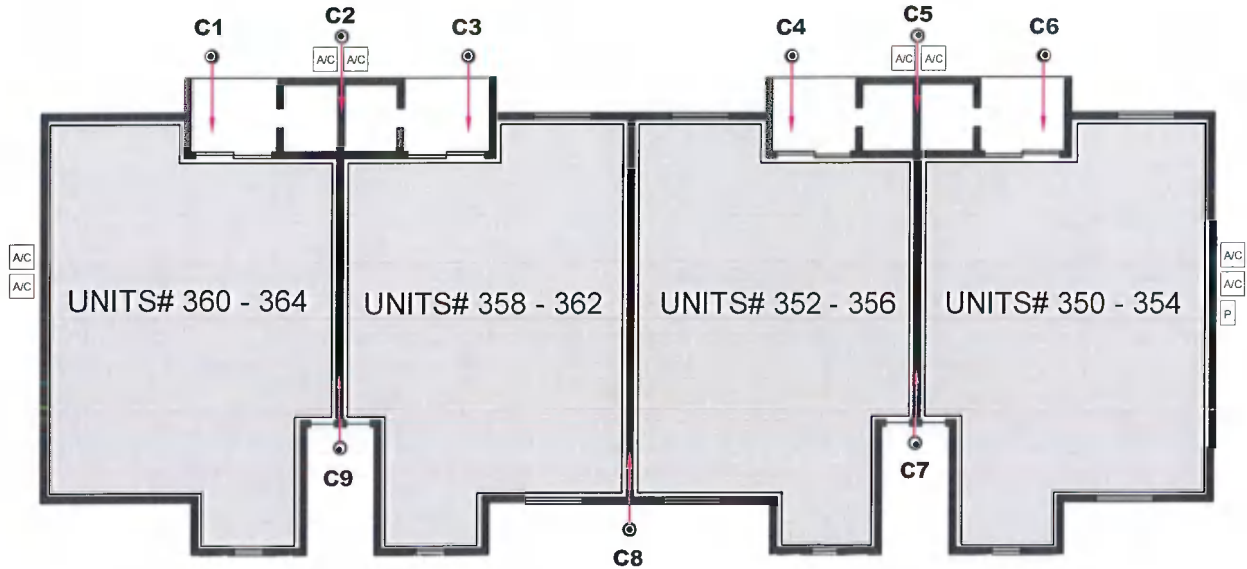

Approximate Scale
1" = 20'



BASIC ENGINEERING

2601 E 7TH AVENUE, TAMPA, FL 33605 | PH: 813-885-4144 * FX: 813-885-4166
WWW.BASIC-ENGINEERING.COM

THE MOORINGS CONDO ASSOC. | BLDG #4
350 - 364 MOORING COVE DRIVE; TARPON SPRING 34689
PINELAS COUNTY

COMPACTION GROUT PLAN

FIGURE NO.: 4c

FILE NO.: B2020-018


DATE: 03/25/2021

CHECKED BY: JJ

TECHNICAL NOTES:

- ✘ - INSTALLED DEPTH: 12', 10', 8', 6', 64' & 2' BGS
- INSTALLED CHEMICAL GROUT POINTS = 12
- INSTALLED CHEMICAL GROUT QUANTITY = 836.7
- NOT FOR PERMITTING

TWO STORY WOOD FRAME BUILDING #4

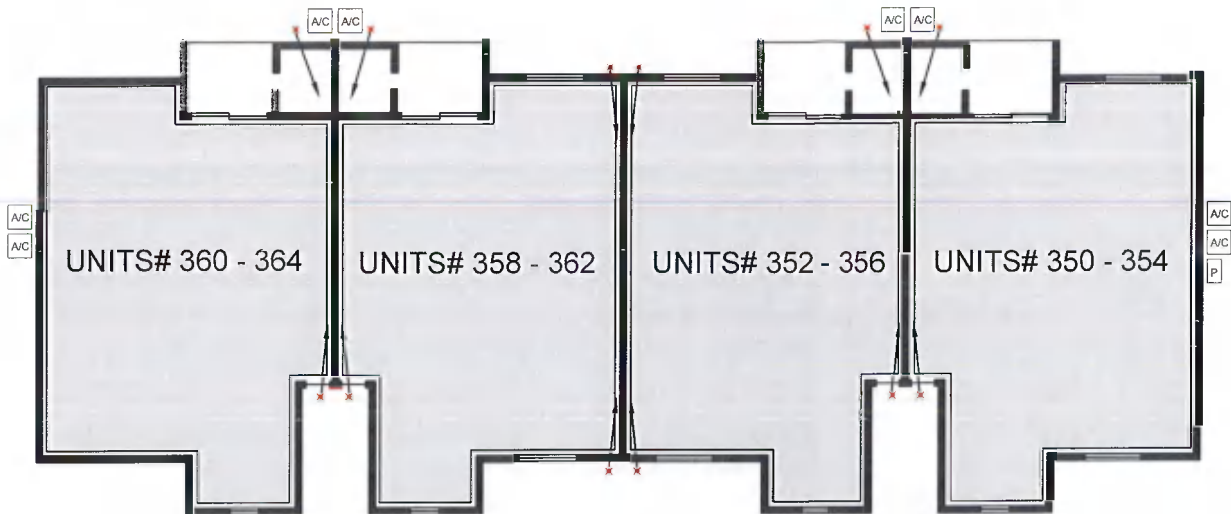

Point #s	Depth (ft)	PSI	Lbs.
1	12	1200	27.4
	10	-	-
	8	-	-
	6	1200	15.1
	4	1200	7.0
2	2	1200	2.8
	12	1200	32.7
	10	-	-
	8	-	-
	6	1200	15.1
3	4	-	-
	2	-	-
	12	1200	50.0
	10	1200	21.1
	8	-	-
4	6	1200	15.1
	4	1200	7.0
	2	1200	2.8
	12	1200	45.1
	10	-	-

Point #s	Depth (ft)	PSI	Lbs.
5	12	1200	16.2
	10	-	-
	8	-	-
	6	1200	8.4
	4	-	-
6	2	-	-
	12	1200	18.6
	10	-	-
	8	-	-
	6	1200	15.1
7	4	1200	4.9
	2	-	-
	12	1200	21.5
	10	-	-
	8	-	-
8	6	1200	4.2
	4	-	-
	2	-	-
	12	1200	50.0
	10	1200	29.9

Point #s	Depth (ft)	PSI	Lbs.
9	8	1200	20.1
	6	1200	15.1
	4	1200	7.0
	2	1200	2.8
	12	1200	50.0
10	10	1200	20.1
	8	-	-
	6	1200	15.1
	4	1200	0.7
	2	-	-
11	12	1200	50.0
	10	1200	29.9
	8	1200	15.8
	6	1200	15.1
	4	1200	7.0
12	2	1200	2.8
	12	1200	37.3
	10	-	-
	8	-	-
	6	1200	10.2
4	-	-	
2	-	-	
Total:			836.7

Approximate Scale

1" = 20'



BASIC
ENGINEERING

2601 E. 7TH AVENUE, TAMPA, FL 33605 | PH: 813-885-4144 * FX: 813-885-4166
WWW.BASIC-ENGINEERING.COM

THE MOORINGS CONDO ASSOC. | BLDG #4

350 - 364 MOORING COVE DRIVE, TARPON SPRING 34689
PINELAS COUNTY

CHEMICAL GROUT PLAN

FIGURE NO.: 4d

FILE NO.: B2020-018

DATE: 03/25/2021

CHECKED BY: JJ
